Name of Work: Package No. 02-(Consists of 5Works) Improvements to Roads and Drains at Hegadenagara Eastern Side Balance Cross Roads in Ward no: 06 Bytarayanapura Sub Division.

Item No.	Items of Work / Description	Unit	Schedule-B	Modified Schedule-B	Executed	% of Work Completed
			Qty	Qty	Qty	
1	Removing and resetting of footpath slab	Sqm	12615.60	12744.61	1163.00	9.12%
8	Earth work excavation by manual means for drains,canals and similar works in all kinds of soils as per drawing and technical specifications, including	Cum	3327.00	5358.80	831.32	15.51%
10	Providing and laying in position plain cement concrete for levelling course for all works in foundation. The granite/trap/basalt crushed graded coarse aggregates	Cum	99.00	45.99	45.99	100.00%
11	Providing and laying in position Reinforced cement concrete for all Foundation works. The granite/trap/basalt crushed graded coarse aggregates	Cum	193.70	101.23	101.16	99.93%
12	Supplying, Fitting and Placing un-coated TMT bar Reinforcement in sub-structure complete as per Drawing and Technical Specifications.(V-III, I.No 13.1	T	13.30	10.98	10.98	100.00%
13	Providing precast slab of 100 mm thick including cost of all materials, labour, curing,transportation,loading ,unloading,etc.,complete as per the direction of	Sqm	3242.30	2385.53	322.91	13.53%
14	Providing and fixing RCC precast cover slab of 230mm thick for drain in cement concrete M20 using graded granite jelly 20mm and down size with steel	Sqm	135.00	28.32	28.32	100.00%
7	Scarifying the existing bituminous road surface to a depth of 50 mm and disposal of scarified material by Mechanical Means using Hydraulic excavator with in	Sqm	5305.00	4251.93	4251.91	99.99%
9	Earth work excavation for Foundation by mechanical means for all works & depth upto 3 m, as per drawing and technical specifications,including setting out,	Cum	4378.60	7457.71	2201.28	29.51%
17	Providing, laying, spreading and compacting graded stone aggregate to wet mix macadam specification including premixing the Material with water at OMC in	Cum	5411.00	6015.60	1587.29	26.38%

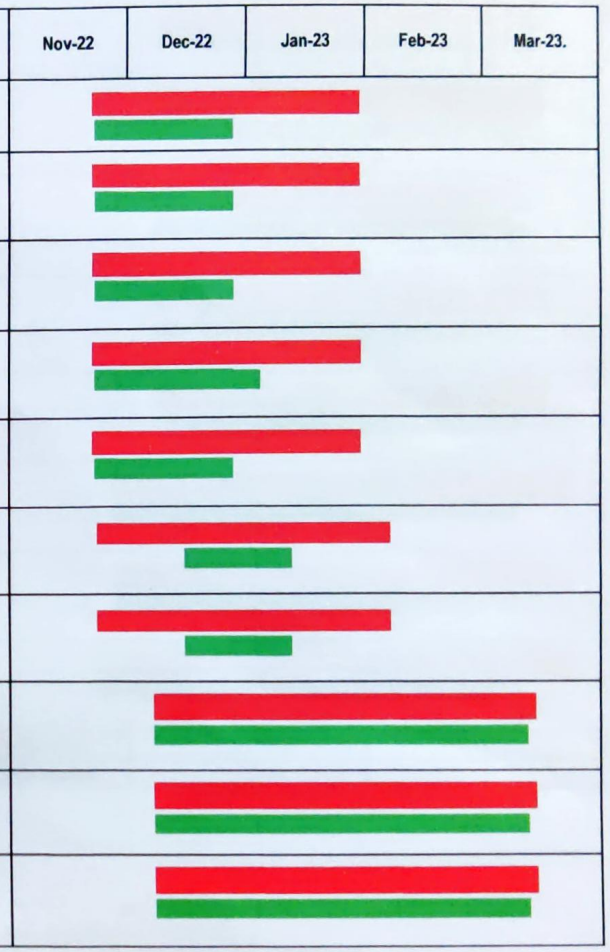

SRAMA Consulting Engineers P. Ltd. Bangalore

ಸಹಾಯಕ ಅಧಿಕಾರಿಯವರು
ಬಿ.ಬಿ.ಎಂ.ಪಿ. ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ

ಸಹಾಯಕ ಅಧಿಕಾರಿ ಎಲೆಕ್ಟ್ರಿಕಲ್
ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ
ಬಿಬಿಎಂಪಿ, ಬೆಂಗಳೂರು-26

Item No.	Items of Work / Description	Unit	Schedule-B Qty	Modified Schedule-B Qty	Executed Qty	% of Work Completed	Nov-22	Dec-22	Jan-23	Feb-23	Mar-23.
18	Providing and applying primer coat with SS1 grade Bitumen Emulsion on prepared surface of granular base including cleaning of road surface and spraying	Sqm	14994.80	22779.30	4251.43	18.66%					
19	Providing and applying tack coat with RS1 Bituminous Emulsion using emulsion pressure distributor at the rate of 0.20 kg/m2 on the prepared bituminous surface cleaned with mechanical broom (P.No.29 It No.5.3	Sqm	64581.80	62885.71	5990.81	9.52%					
20	Providing and laying Dense Graded Bituminous Macadam with 40/60 TPH capacity HMP using crushed aggregates of specified grading, premixed with bituminous binder VG-30, @ 4.5 per cent by	Cum	1139.00	1139.09	212.60	18.66%					
21	Providing and laying Bituminous Concrete with 40/60 TPH capacity hot mix plant using Crushed aggregates of specified grading, premixed with bituminous binder VG-30, @ 5.4 per cent of mix and filler, transporting	Cum	2580.20	2515.43	239.30	9.51%					
22	Providing and laying of hot applied thermoplastic compound 2.5 mm thick including reflectorising glass beads @ 250 g/ m2 area, thickness of 2.5 mm is	Sqm	1888.00	1870.48	195.40	10.44%					
23	Providing and laying in position plain cement concrete for levelling course for all works in foundation. The granite/trap/basalt crushed graded coarse aggregates	Cum	569.60	325.27	202.08	62.12%					
24	Providing and constructing un-reinforced plain cement concrete pavement, thickness as per design, over a prepared sub base, with 43 grade cement or any other	Cum	569.60	325.27	202.08	62.12%					
25	Cost of Haulage Excluding Loading and Unloading Taking output 25 t load and lead 10 km = 250 t.km (Vol-III) Page No.3, Item No.1.4C of PWD SR 2021-22	T.km	9601.40	16391.97	3881.72	23.68%					
							Planned				
							Executed				

SHIPRAMA Consulting Engineers Pvt. Ltd. Bangalore

Assistant Engineer
Ward no. 06
ಬಿ.ಬಿ.ಎಂ.ಪಿ ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ

Asst.Executive Engineer
Byatarayanapura Sub Division, B.B.M.P
ಬಿ.ಬಿ.ಎಂ.ಪಿ., ಬೆಂಗಳೂರು-26
